




2025

5th St. S to 4th St. N.

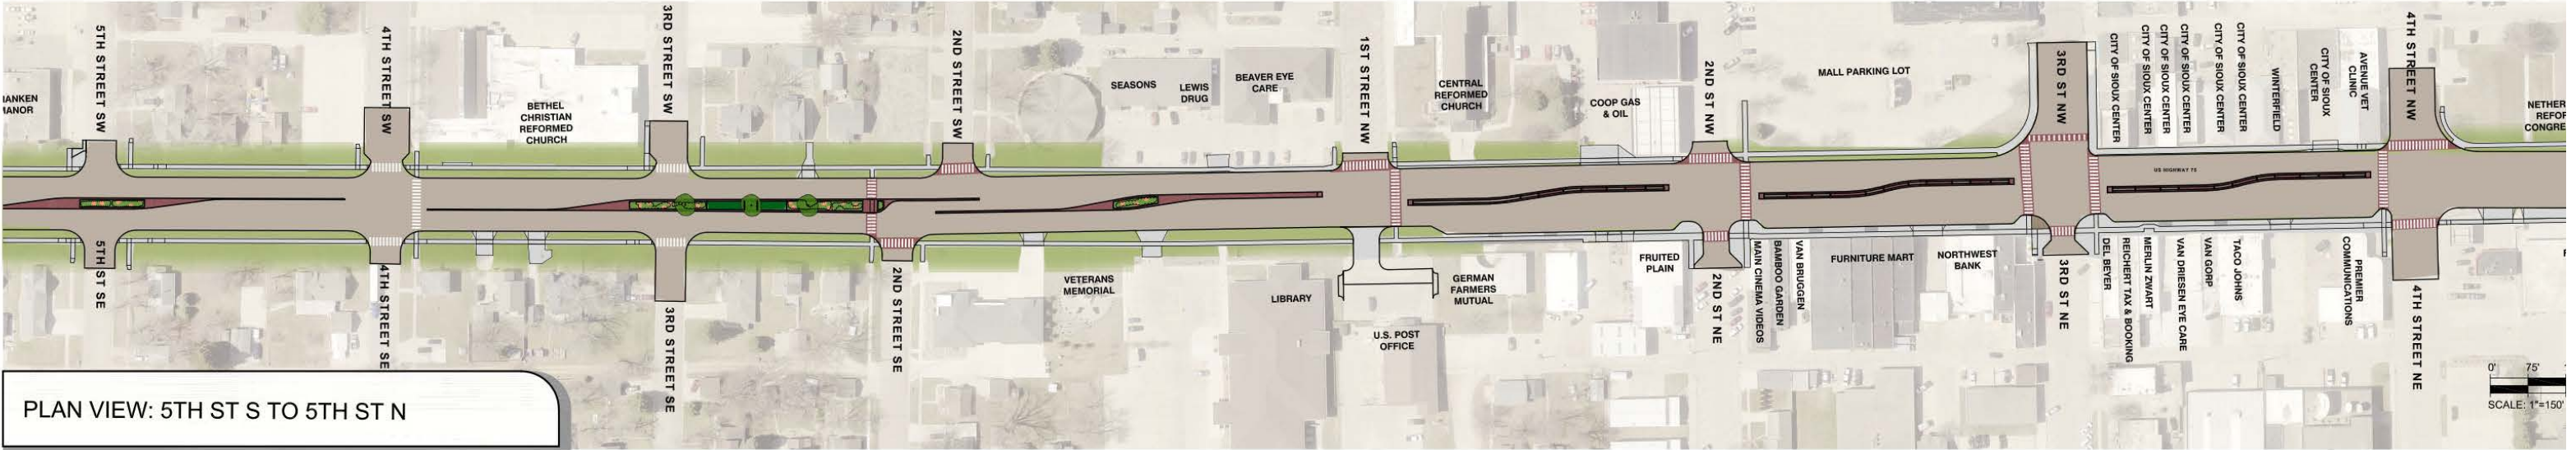

2026

4th St. N to 12th St. N.



2025 Design



2025 Design



2025 Design



2025 Design




2025 Design



2025 Design



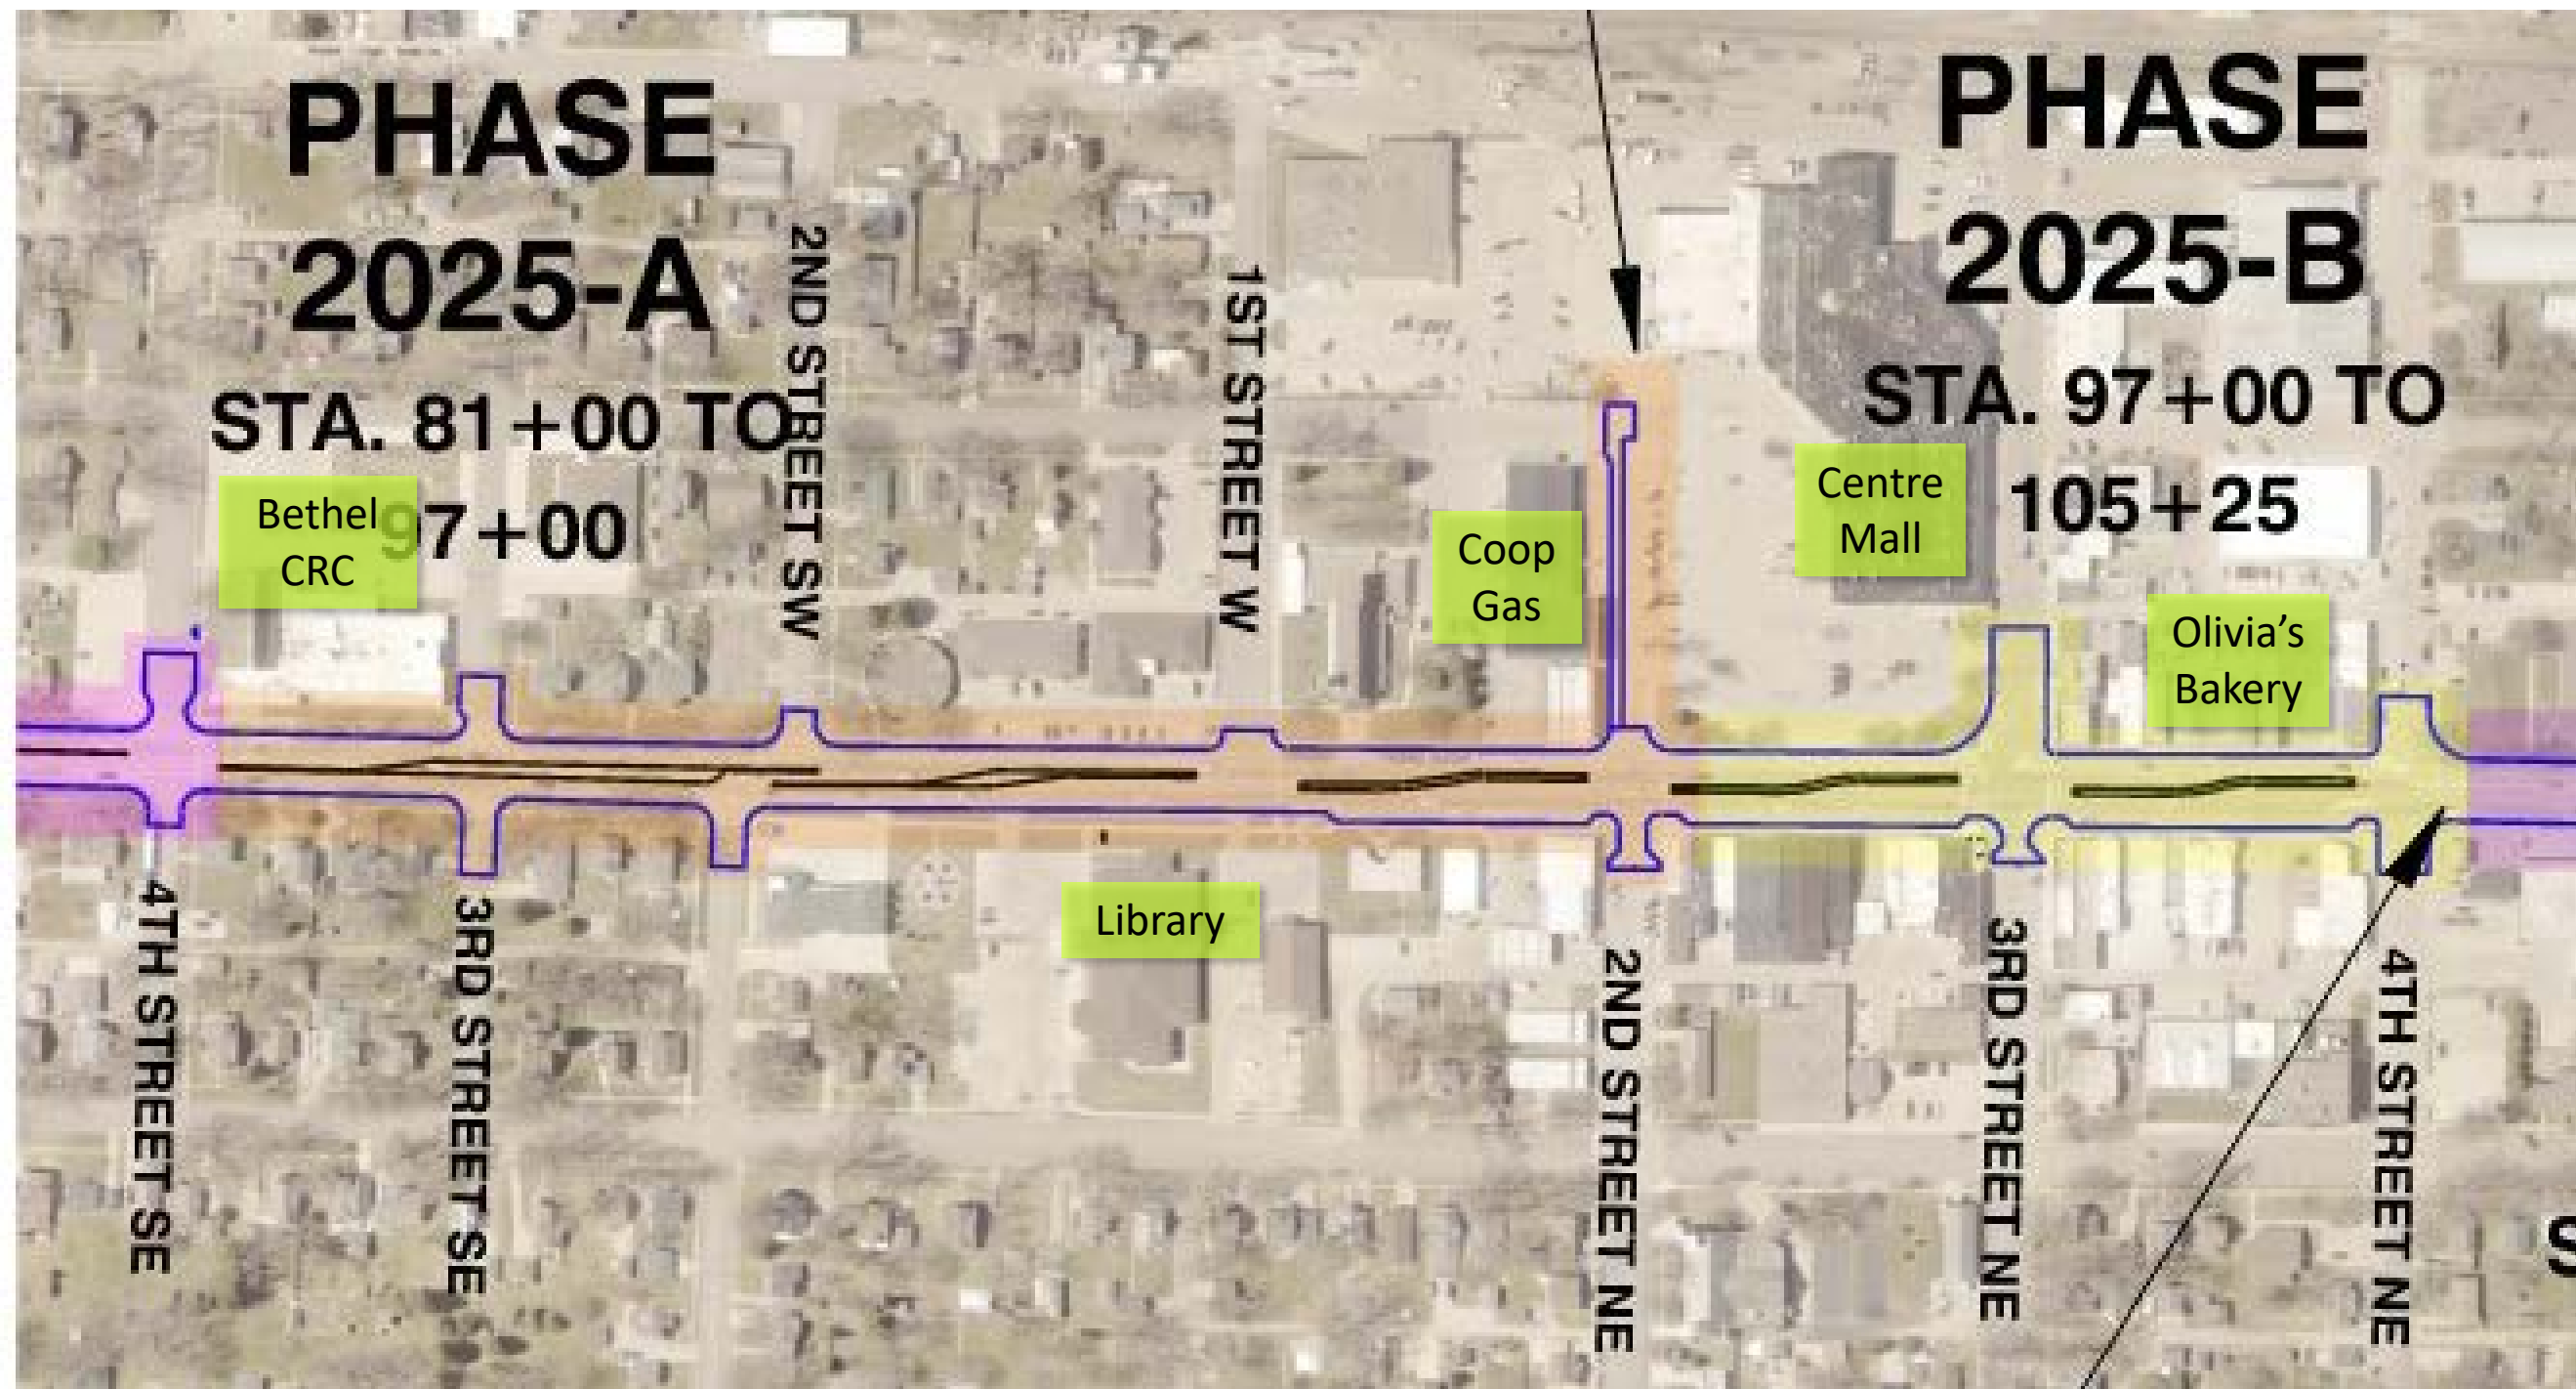

- Full closures this year for Highway 75: *(these may overlap)*
 - 2nd St. SE to 2nd St N • 5th St. S to 2nd St. S • 2nd St. N to 4th St. N
- Soft closures will be set up outside these areas, but still allow local traffic

2025 Construction stages



Beginning in March

- Storm sewer install north of Coop Gas (2nd St. NE)
- Water main install on west side of Highway 75
 - lane closure from 5th S. to 3rd S.


2025 Construction stages



Water main install on east side Hwy 75

- lane closure from 5th S. to 3rd S.


2025 Construction stages

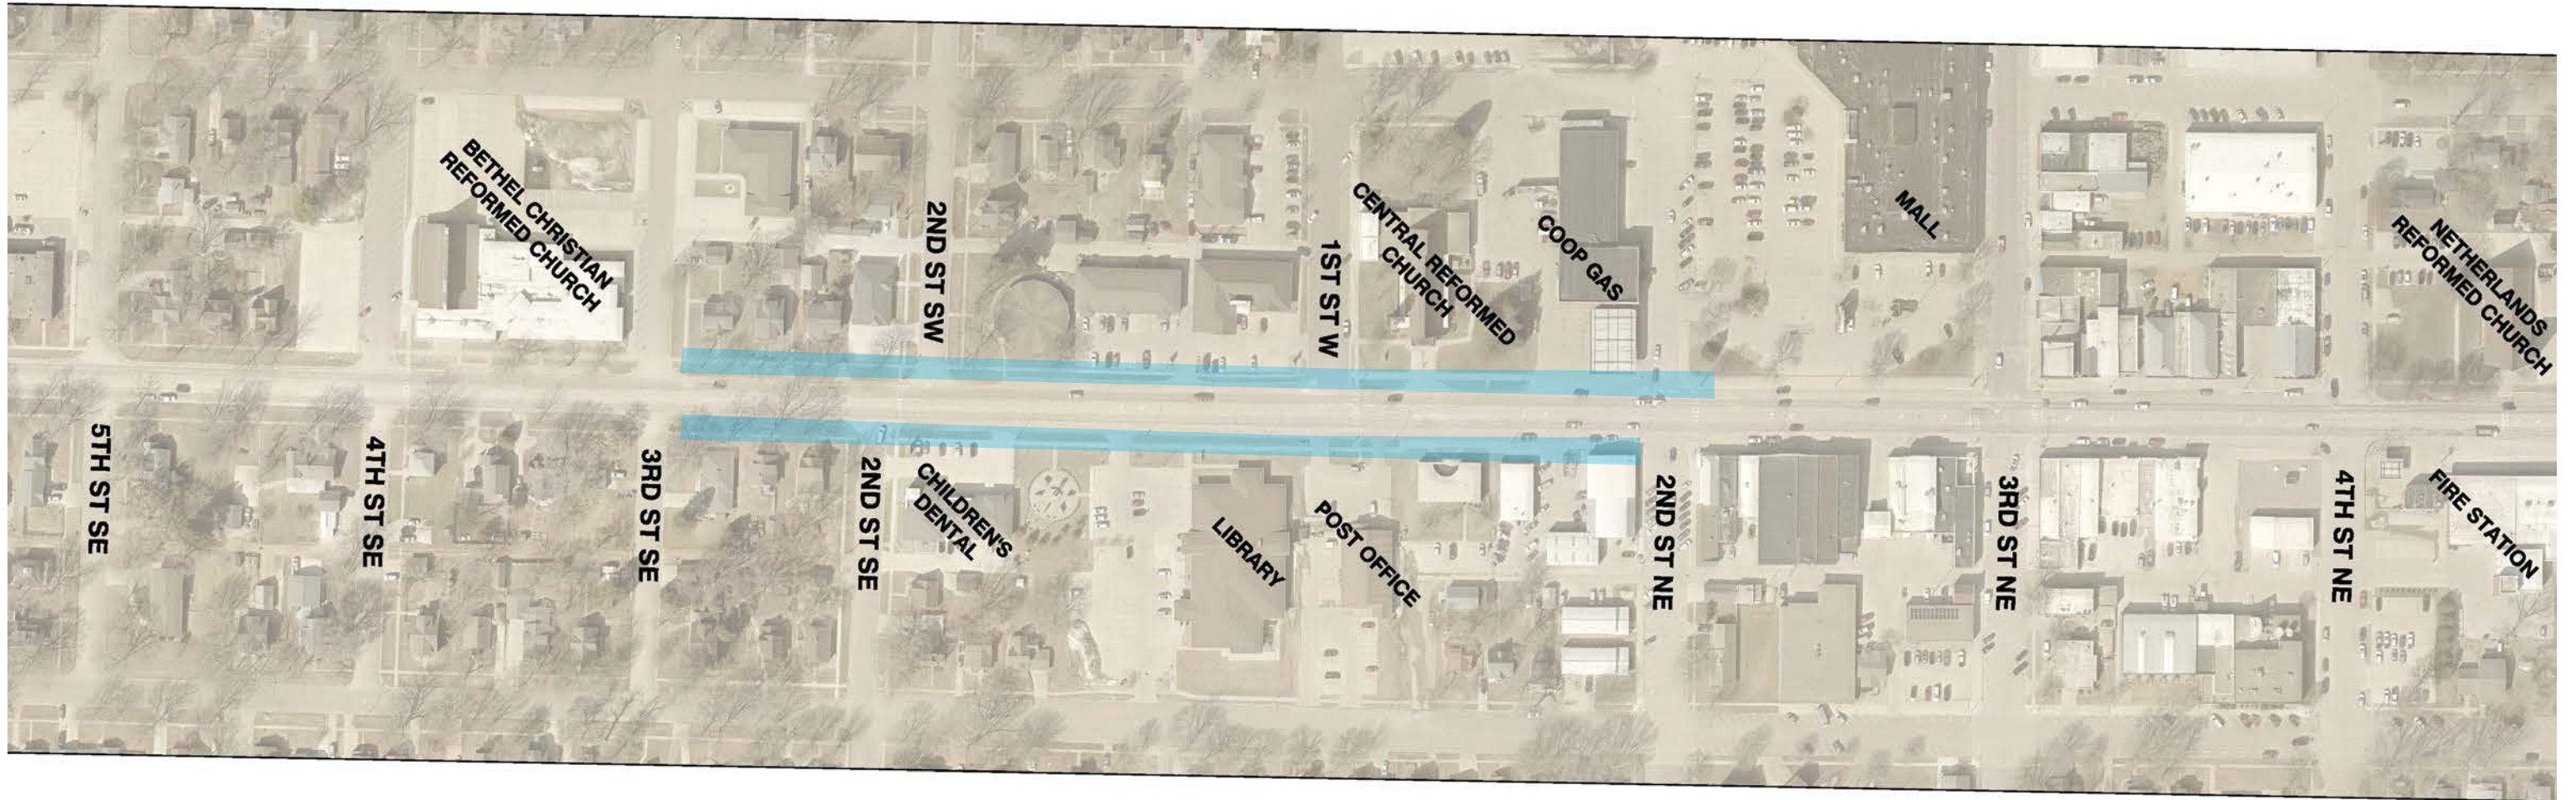

In April, full closure will begin

- Water main install continues on both sides of Highway 75 to 2nd St. N

2025 Construction stages

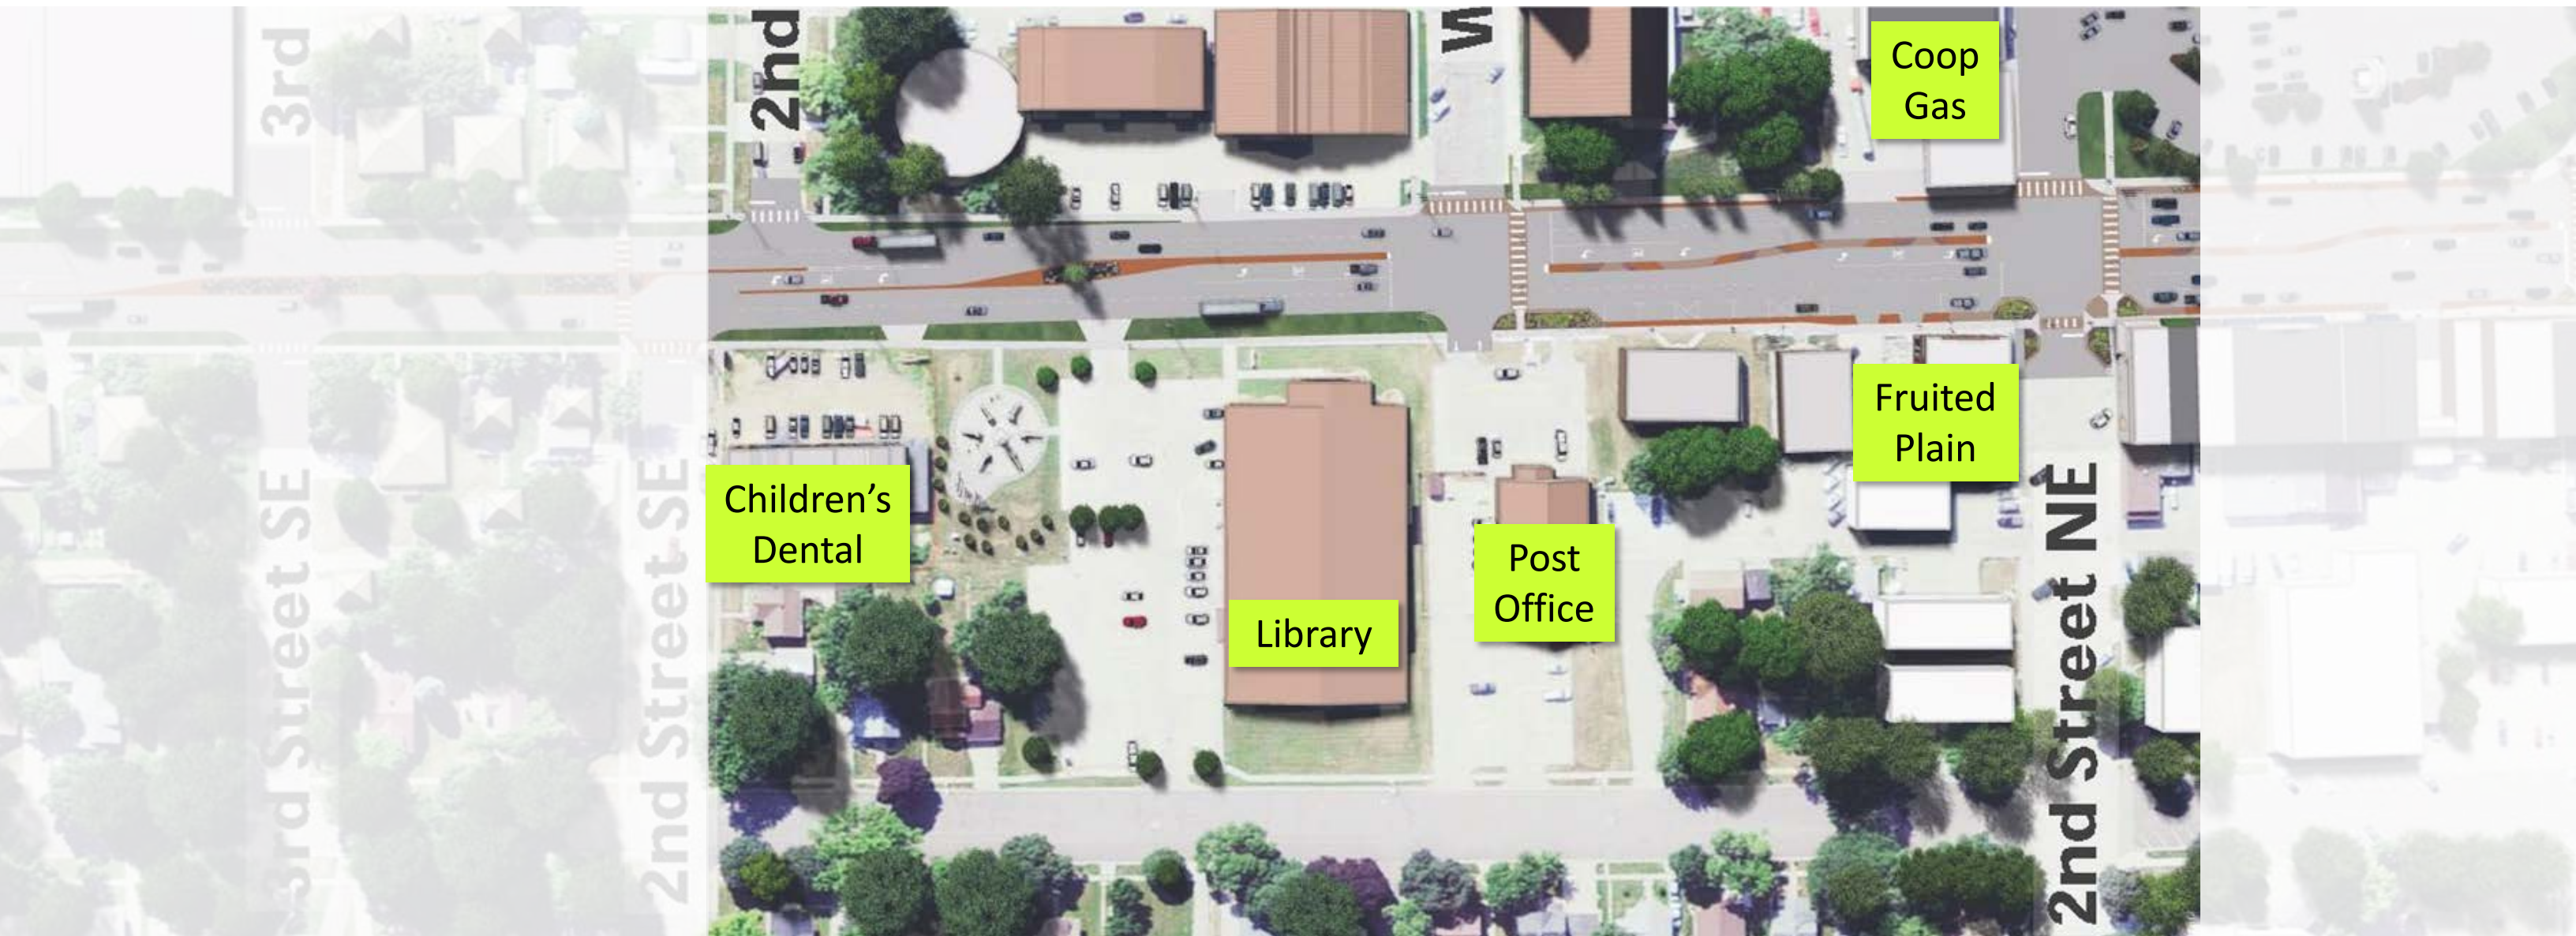


2nd Street SE to 2nd Street N

- Pavement removal
- Underground utilities (2nd St. N is low point)

- Resurface
- Sidewalks, medians, landscape

2025 Construction stages

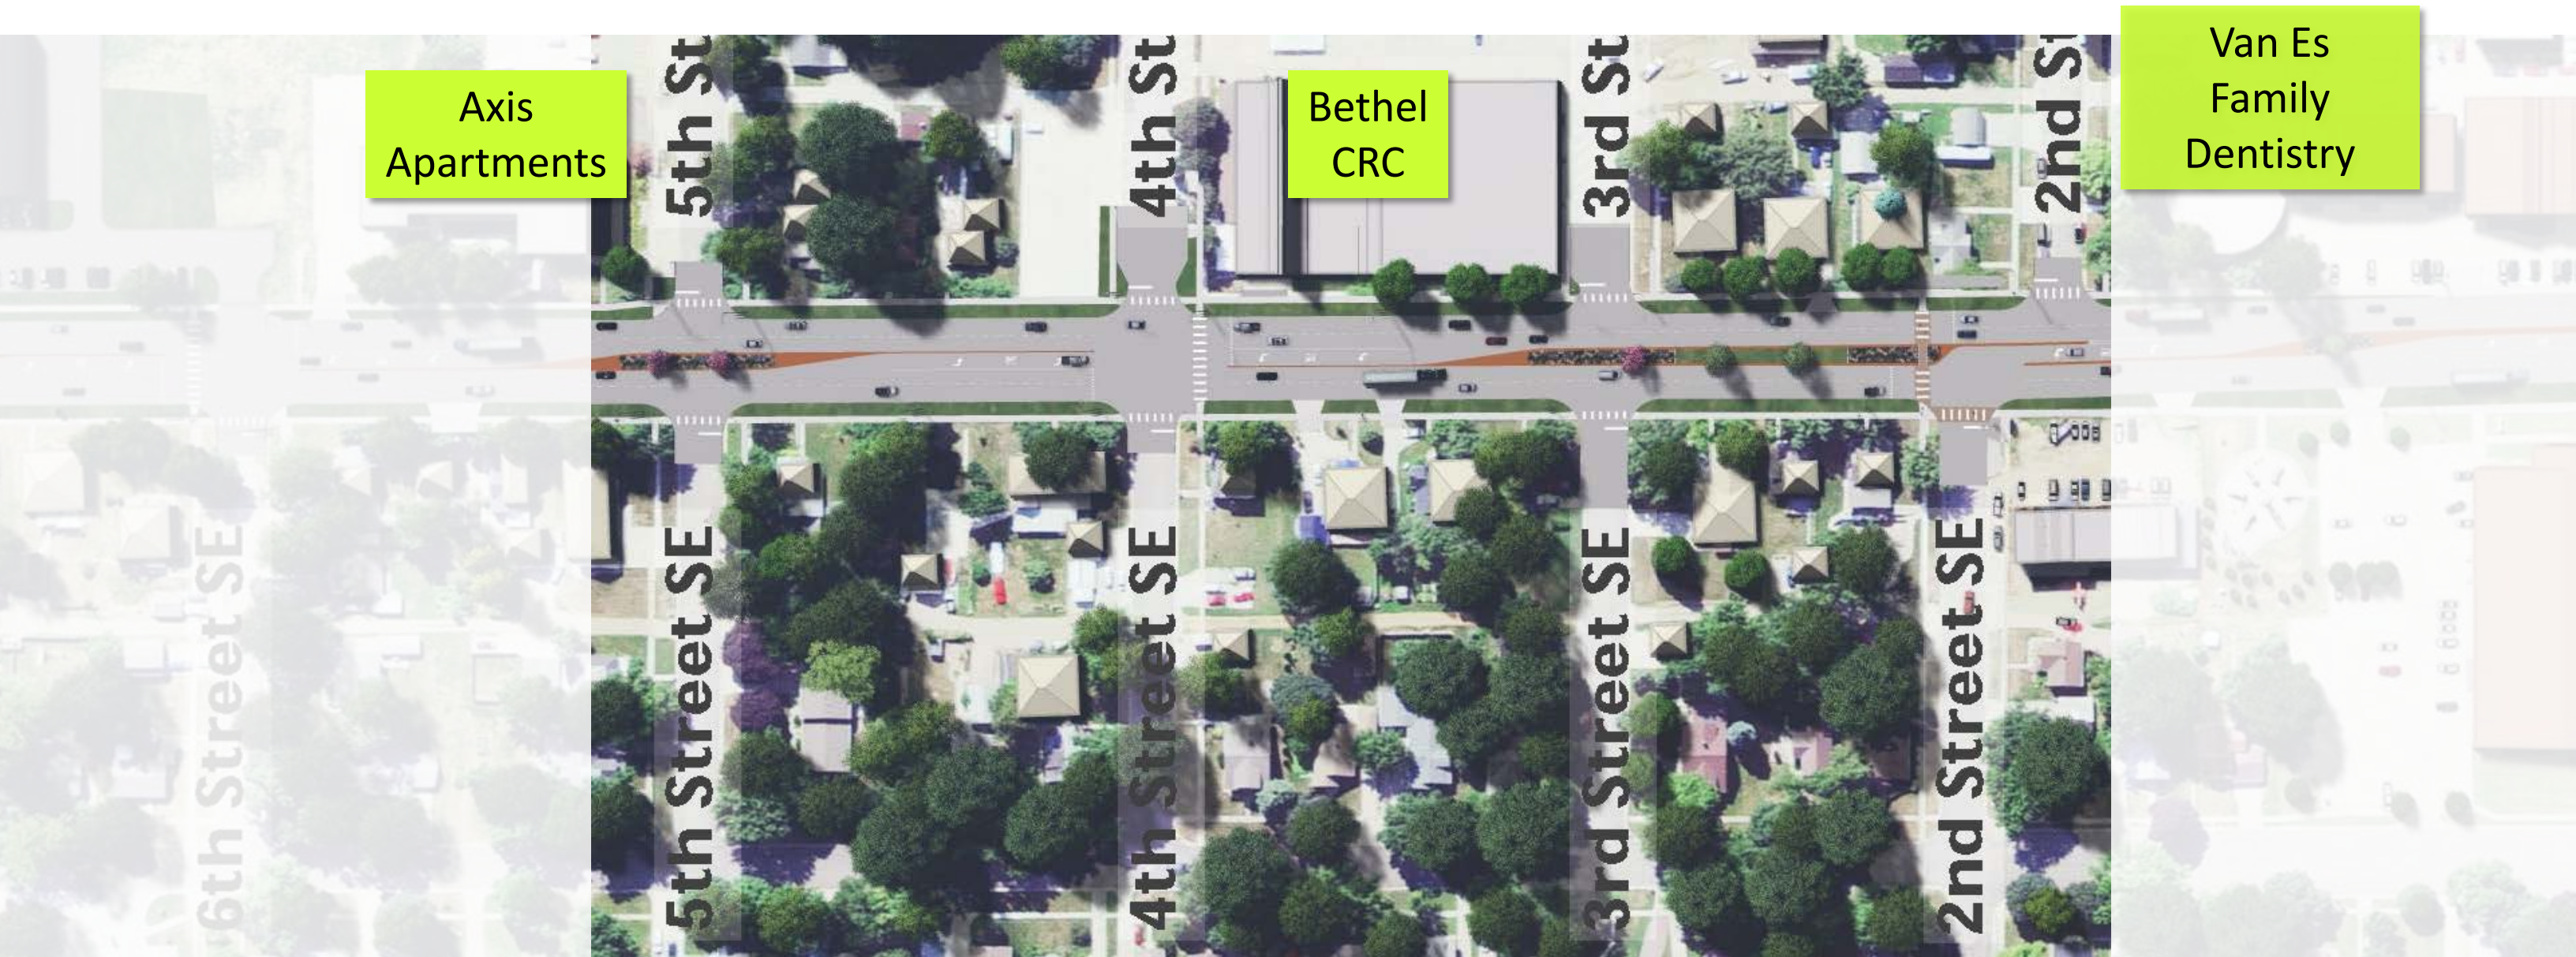

5th Street S to 2nd Street SE

- Street pavement removal
- Underground utilities
- Resurface
- Sidewalks, medians, landscape




2025 Construction stages



2nd Street N to 4th Street N

- Water main install
- Street pavement removal
- Underground utilities
- Resurface
- Sidewalks, medians, landscape

2025 Construction on side streets

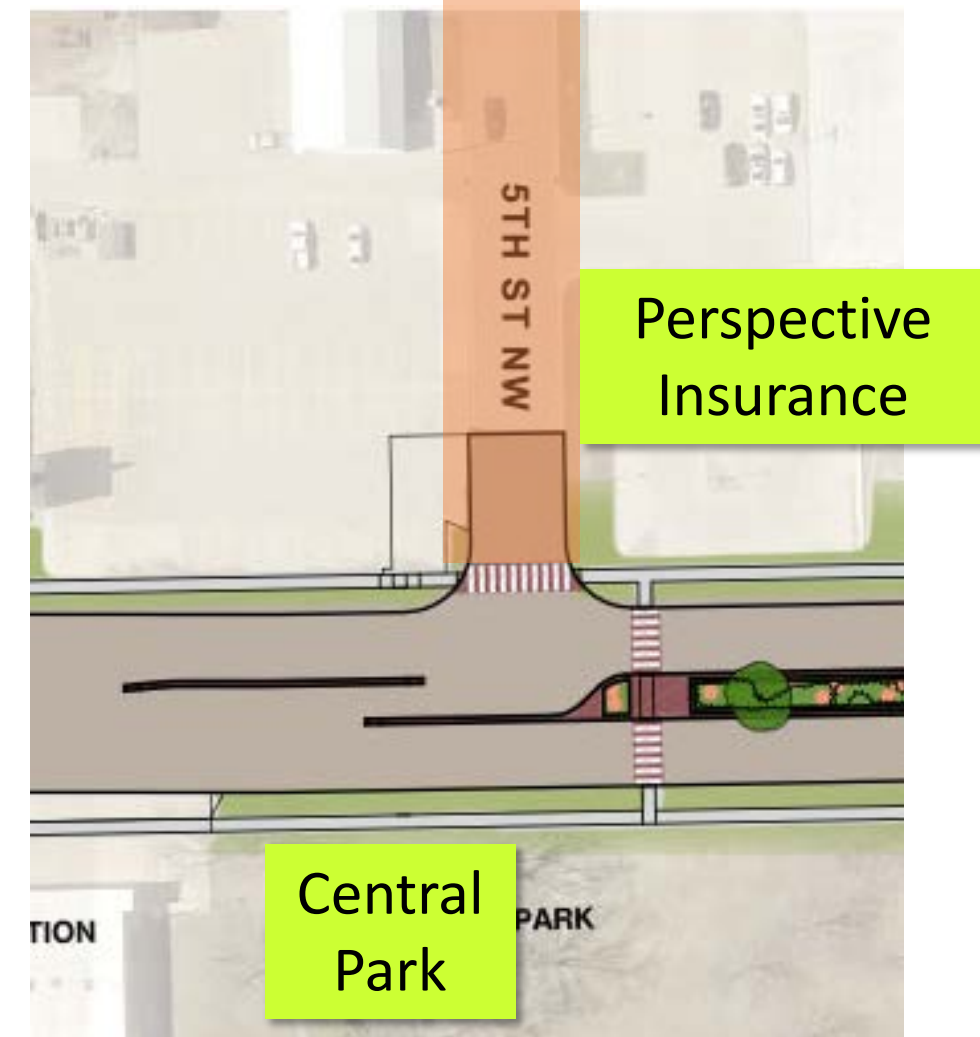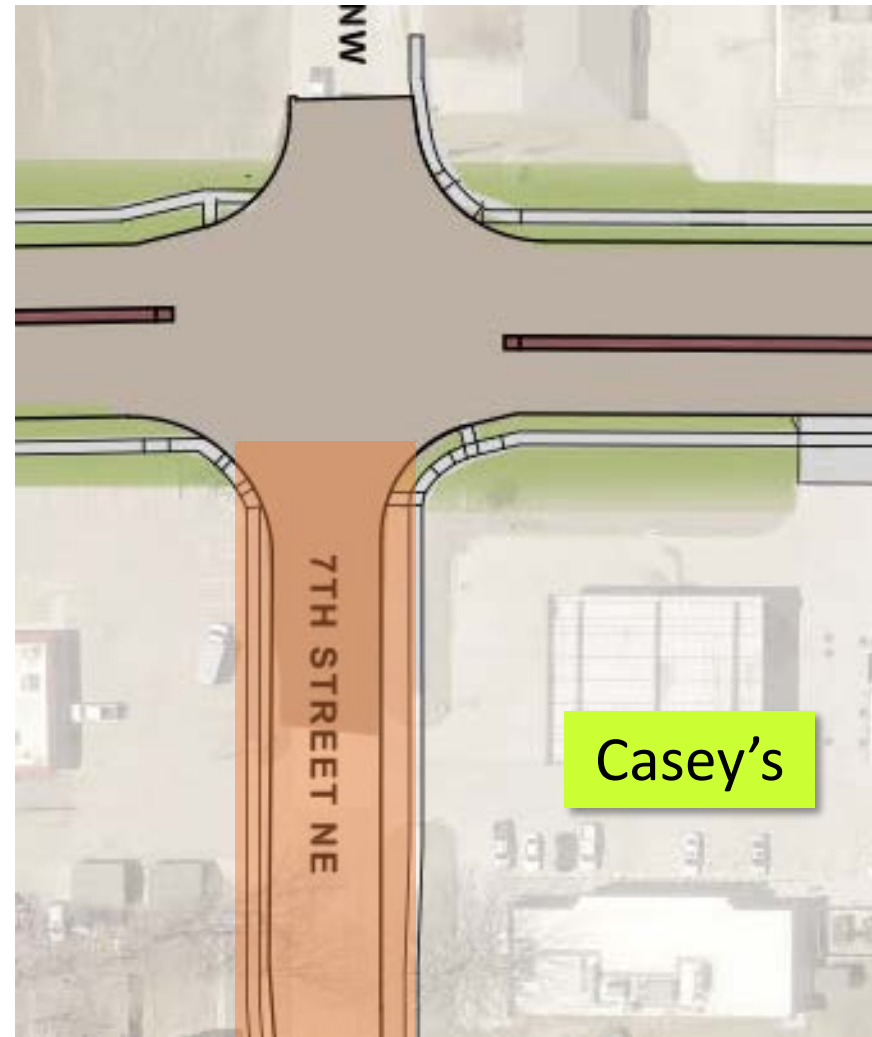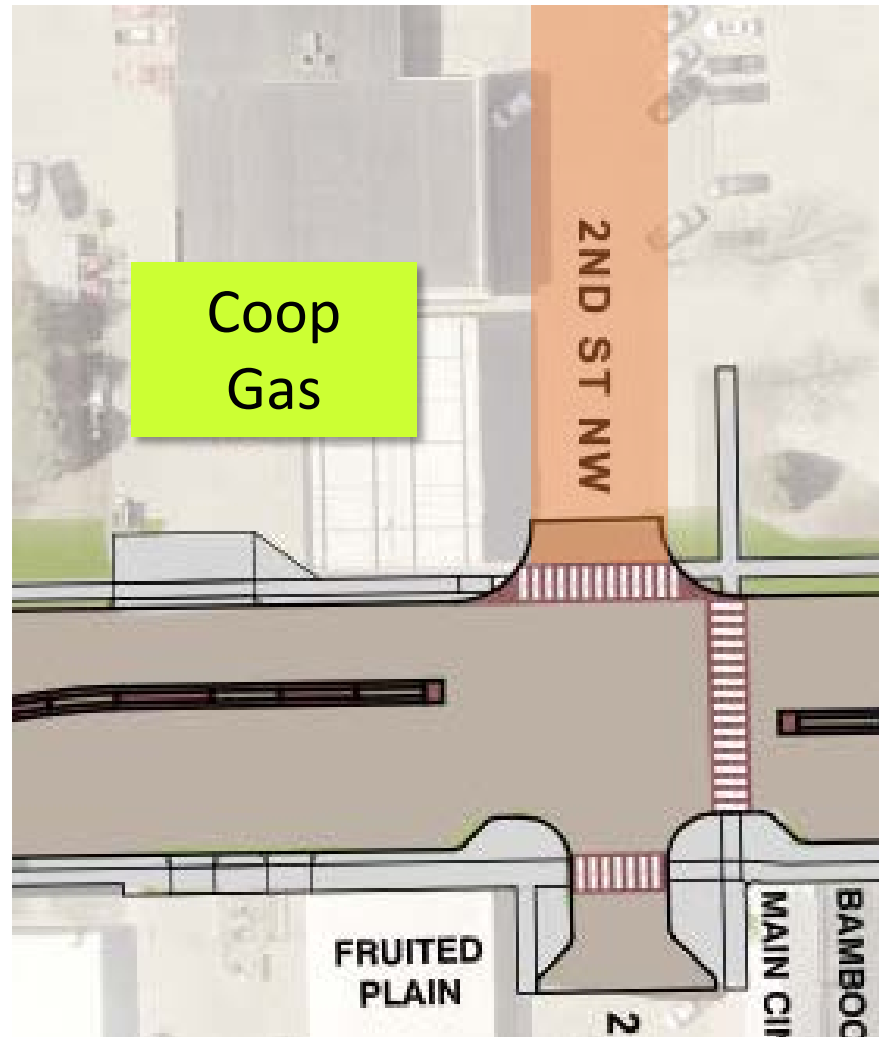

- 2nd Street NW storm sewer
- 7th Street NE water main and street paving
- 5th Street NW storm sewer

